


VISUAL SOIL INSPECTION REPORT

S'ALAAH'UDDIN SCHOOL, HULHUMALE PHASE-2


Date: 3-AUGUST-2020

Pit depth: 1900mm

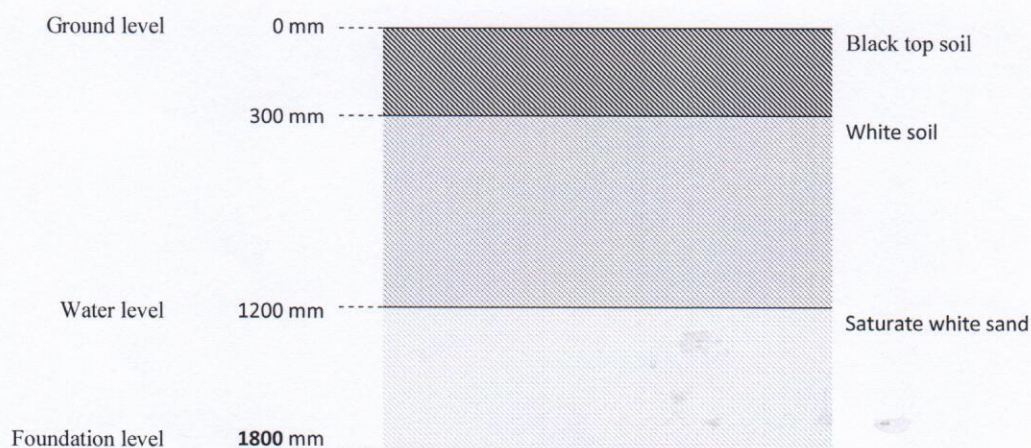

Coral pieces were encountered at the test pit. The estimated soil bearing pressure is at 150 N/mm²

All existing foundation structures to be completely removed. Foundation to be laid 1.8m below ground level. Dewatering will be required.


Mariyam Samah
B. Civil Engineering (Hons)
ArchEng Studio

